


Kintyre to Hunterston Link Progress Update October

Work Schedule:

Start date: 23rd October

Duration of Works: 6 Weeks

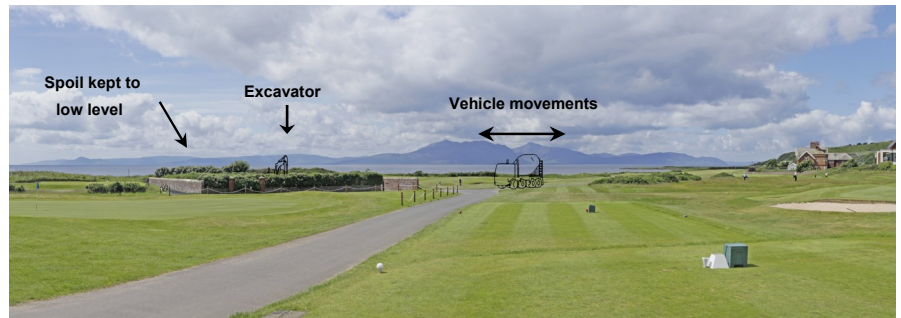

Completed Works -

- Minor improvements to access road
- Construction of new greens material storage area and relocation of existing materials in Holland House
- Complete removal of materials to new storage area
- Site set up to receive drilling rig

Planned Works: 23rd October - 27th November

- Plant and site welfare facilities delivered to the Holland House area, site set up complete including fencing and signage
- Commencement of drilling works
- Duration of drilling works altered to allow for expected ground conditions

1st - 2nd December

- Site Decommission

Golf Course Disruption - There will be minor disruption to the golf course:

- Vehicle movements on the access road estimated at an average of two per hour for the working day
- Holland House area no longer accessible to the public
- Noise disruption from the operation of the drilling rig.
- Foot access on to the course at regular intervals to monitor location and depth of drill

Contact details for the project

Contact: Karen MacGregor

Community Relations Major Projects Tel:0751 646 1129 Email: WestKilbrideProjects@spenergynetworks.com

More information Visit: www.spenergynetworks.com/investinginthenetwork
www.ssepd.co.uk/KintyreHunterston
www.westernhvdclink.co.uk
