


# Kintyre to Hunterston Link Progress Update October

## Work Schedule:

Start date: 23rd October

Duration of Works: 6 Weeks

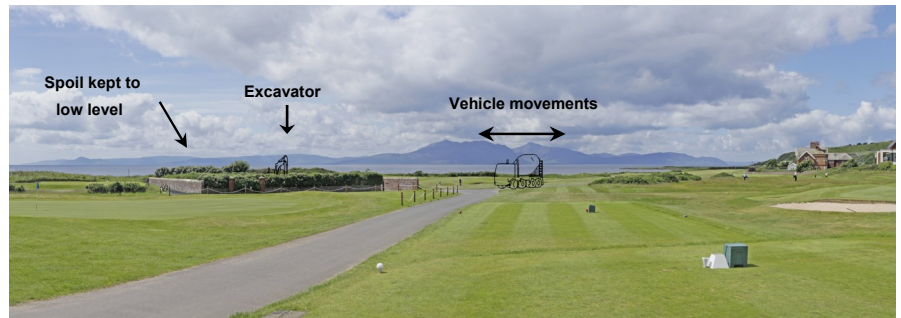

## Completed Works -

- Minor improvements to access road
- Construction of new greens material storage area and relocation of existing materials in Holland House
- Complete removal of materials to new storage area
- Site set up to receive drilling rig

## Planned Works: 23rd October - 27th November

- Plant and site welfare facilities delivered to the Holland House area, site set up complete including fencing and signage
- Commencement of drilling works
- Duration of drilling works altered to allow for expected ground conditions

## 1st - 2nd December

- Site Decommission

## Golf Course Disruption - There will be minor disruption to the golf course:

- Vehicle movements on the access road estimated at an average of two per hour for the working day
- Holland House area no longer accessible to the public
- Noise disruption from the operation of the drilling rig.
- Foot access on to the course at regular intervals to monitor location and depth of drill

## Contact details for the project

**Contact:** Karen MacGregor

Community Relations Major Projects Tel:0751 646 1129 Email: [WestKilbrideProjects@spenergynetworks.com](mailto:WestKilbrideProjects@spenergynetworks.com)

**More information Visit:** [www.spenergynetworks.com/investinginthenetwork](http://www.spenergynetworks.com/investinginthenetwork)  
[www.ssepd.co.uk/KintyreHunterston](http://www.ssepd.co.uk/KintyreHunterston)  
[www.westernhvdclink.co.uk](http://www.westernhvdclink.co.uk)
